


STANWOOD-CAMANO SCHOOL DISTRICT

BOARD UPDATE

December 1, 2020

New Stanwood High School Project Schedule

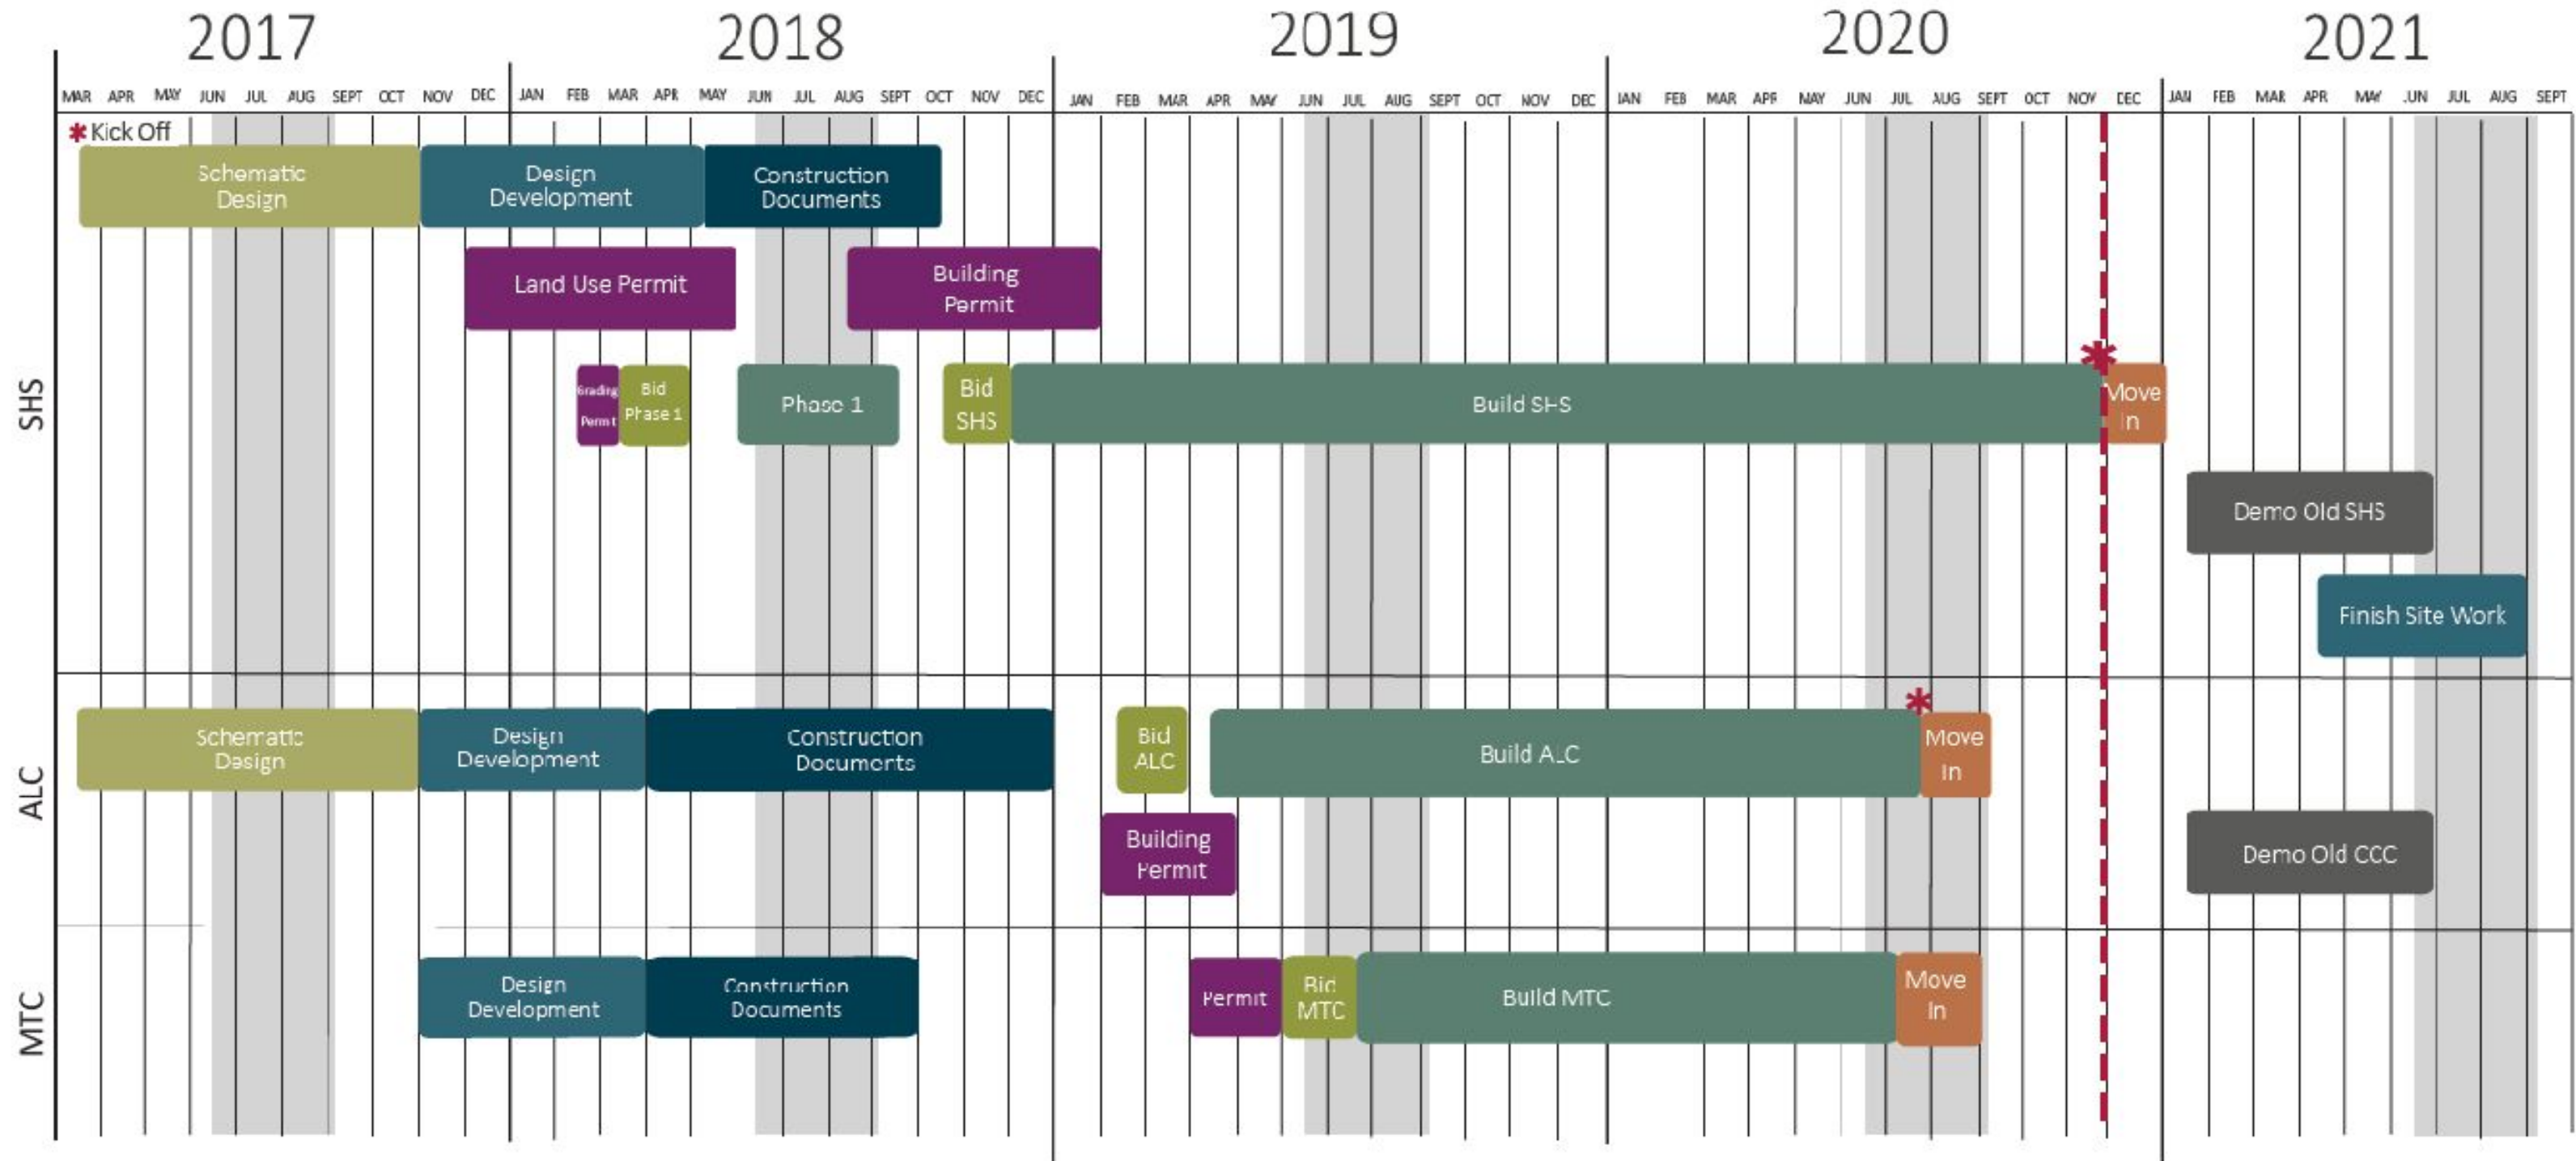

SCHEDULE

STANWOOD-CAMANO SCHOOL DISTRICT
 STANWOOD HIGH SCHOOL AND ALTERNATIVE LEARNING CENTER
 11 APRIL 2019

SHS Move:

- ✓ Teachers and staff are busy packing up their classrooms and offices.
- ✓ Bekins movers will be moving SHS in two (2) phases.

Phase I (Nov. 30 – Dec. 2) – focus on:

- ✓ Moving the PAC costumes, sets, and other teacher materials.
- ✓ Moving physical education and athletic equipment.
- ✓ Moving library books, materials, and supplies.
- ✓ Moving wood, metal, and mechanics shop (CTE) equipment and classroom materials.
- ✓ Moving selected items of existing furniture and equipment from SHS and Church Creek Campus school areas.

Phase II (Dec. 16 – Dec. 18) – focus on:

- ✓ Moving teacher classroom materials to the correct new rooms.
- ✓ Moving administration area equipment, files, and supplies.

SHS Furniture Installation:

- Saxton Bradley will be providing the bulk of the school furnishings through a KCDA contract.
- Classroom desks and chairs will be on site December 6th or 7th, depending on how quickly the freight is processed at the port and will take the week to place.
- Office furniture, soft furniture and file cabinets will be installed the week of December 14th.

SHS Construction Progress:

Interior

- Painting is 95% complete. Touchup is ongoing.
- Commissioning is going well and is 85% complete.
- PAC stage floor in process. This was started a bit late because of supply issues with the floor lighting.
- Fire alarm and sprinkler testing is complete and signed off. Fire Pump testing is scheduled for the first week of December.
- Final cleaning is commencing.
- Ballfields are on the final layer and adjacent concrete and fencing work is in progress.
- SCSD IT has been on site to start their work in the MDF/IDF's and hanging clocks.

Exterior

- Bus and staff parking lot is complete.
- Landscaping at main building and along 72nd is complete.
- Window cleaning starts this week.

SHS Demo Information:

- Abatement/Demolition is scheduled to start in January 2021.
- Abatement will take approximately four to six weeks.
- Demolition will take approximately eight to twelve weeks.
- SHS existing building site will be fenced off and all student traffic between SHS and CCC will be routed along 272nd.

ALC Construction Progress:

- Students and staff have occupied the school.
- Punch list work is being completed.
- Colacurcio will have someone on site during the interim between CCC completion and building demolition.
- Commissioning is 90% complete.
- Blower door tests (energy code requirement) passed easily.

ALC Demo Information:

- Colacurcio will have 15 weeks to substantially complete their work on site once abatement starts.
- Abatement will take four to five weeks.
- Demolition will take four to five weeks.
- Remaining site work will take four to five weeks.

MTC Progress:

- The Punch List is nearing completion.
- A few furniture and equipment pieces are still on order and should arrive within the next few weeks.
- The completed project will go to the Board for final acceptance, probably in December/January.

Financial Update:

- Status of State Matching Funds for ALC & SHS.
- Cash Flow Update.
